


WOLLONGONG EDM TESTLINE

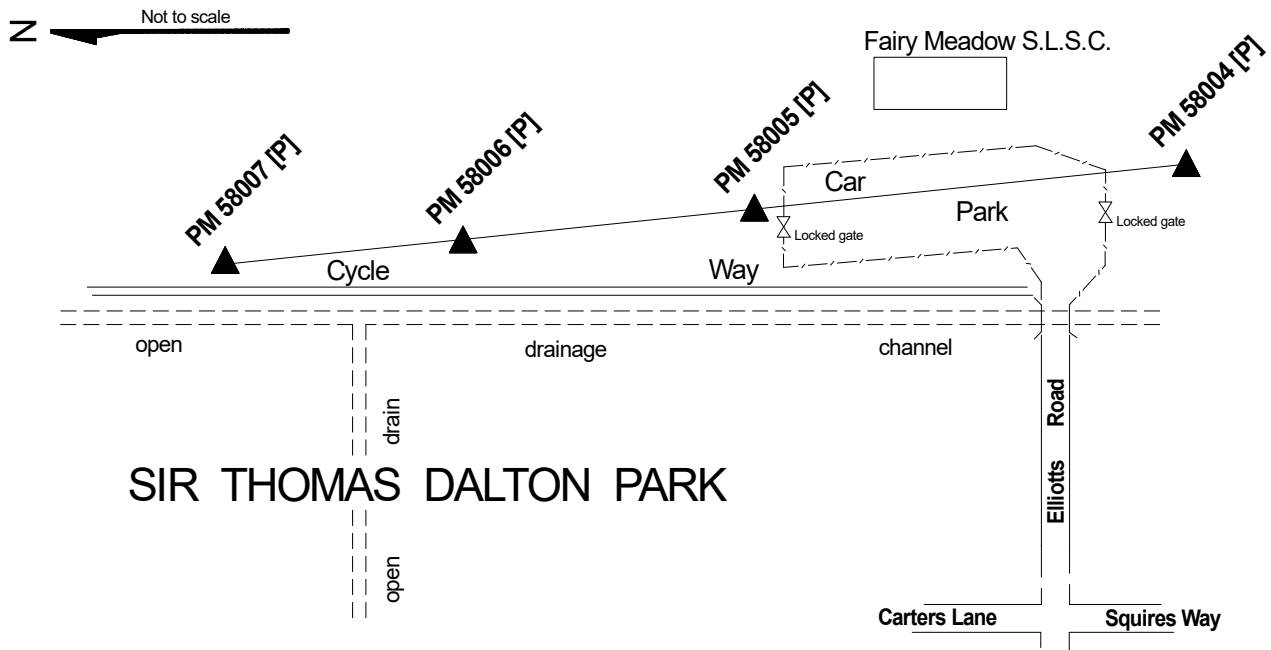

Authorised access only - For baseline booking & to obtain security code to padlock: www.spatial.nsw.gov.au/edmbooking (10mm Allen key required to remove pillar caps.)

HORIZONTAL DISTANCES (metres) at datum 5.942m AHD

From	To	Distance	Mark	RL (AHD) *
PM 58004	PM 58005	194.9670	PM 58004	7.425
PM 58004	PM 58006	417.4719	PM 58005	6.423
PM 58004	PM 58007	599.9687	PM 58006	5.942
			PM 58007	6.724

*The Reduced Levels (metres) were not determined at this date and are on an approximate AHD datum. These height measurements are outside the NATA Scope of Accreditation.

Method of verification: Surveyor-General procedure VA-QMS-01

Reference instrument used : Leica TS 30, Serial No. 360783
 Verified in accordance with Regulation 13 of the National Measurement Regulations 1999.

Uncertainty of distances: +/- (0.8 + 1.3 x 10⁻³L) mm, L= length in metres
 This uncertainty is calculated in accordance with the principles of the ISO Guide to the Expression of Uncertainty in Measurement, with an interval estimated to have a confidence level of 95% and a coverage factor of 2. The uncertainty applies at the time of measurement only and takes no account of pillar movement that may occur after the date of verification.



Accredited for compliance with ISO/IEC 17025 - Calibration
 All equipment used is calibrated by NATA accredited laboratories, and the measurements included in this document are traceable to SI units.
 This document shall not be reproduced, except in full.
 NATA Accredited Laboratory Number: 14965

R K Lock date: 18/12/23
 Senior Surveyor
 (Legal Metrology Officer)
 for the Surveyor-General of NSW

Date of Verification: 06 December 2023
