




TAREE EDM TESTLINE

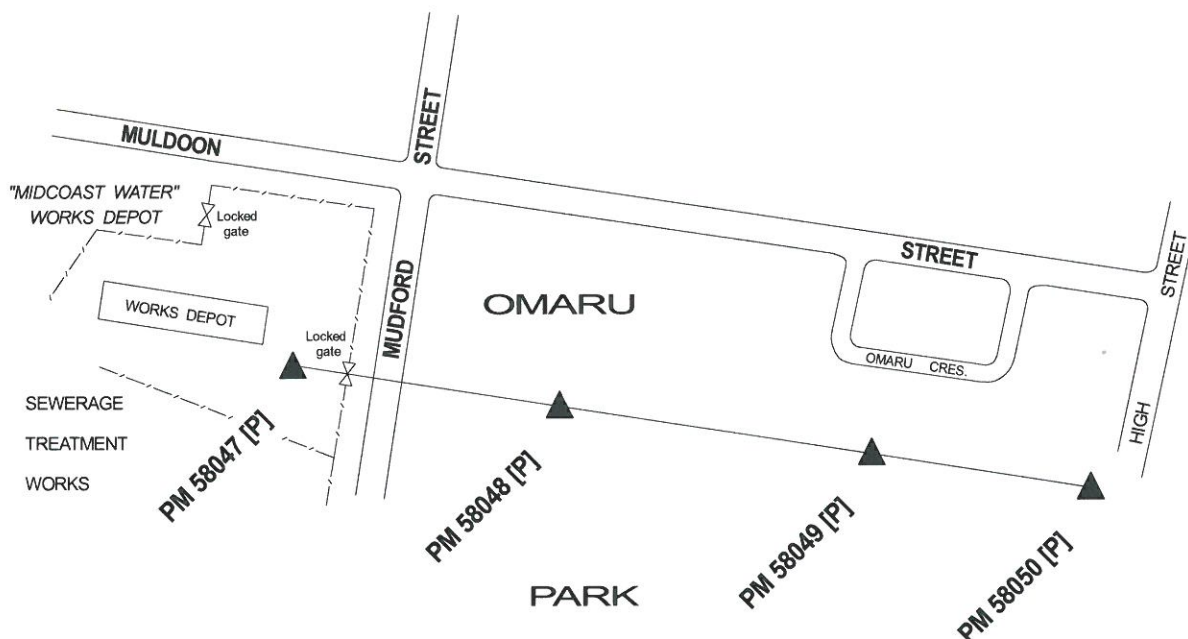

ACCESS : If gates are locked phone "Midcoast Water" for access. ph. 6592 4801

(3/8" Allen key required to remove pillar caps)

HORIZONTAL DISTANCES (metres) AT DATUM 6.045 m AHD

From	To	Distance	Mark	RL (AHD) *
PM 58047	PM 58048	158.839	PM 58047	9.375
PM 58047	PM 58049	374.507	PM 58048	6.045
PM 58047	PM 58050	515.039	PM 58049	7.454
			PM 58050	10.659

*The Reduced Levels (in metres AHD) were not re-verified at this date.

Method of verification: VA-QM-01 and NMI's Verifying Authorities Handbook, 2nd Ed. November 1988

Distances by the Surveyor-General of NSW, in accordance with the verification of a Reference standard of length as prescribed by the National Measurement Act 1960.

Instrument used : Leica TS 30, Serial No. 360783

Verified in accordance with Regulation 13 of the National Measurement Regulations 1999

Uncertainty of distances: $\pm (0.5\text{mm} + 1.3\text{ppm})$

This uncertainty is calculated in accordance with the principles of the ISO Guide to the Expression of Uncertainty in Measurement, with an interval estimated to have a confidence level of 95% and a coverage factor of 2. The uncertainty applies at the time of measurement only and takes no account of pillar movement that may occur after the date of verification.



Accredited for compliance with ISO/IEC 17025.

The results of the tests, calibrations and/or measurements included in this document are traceable to Australian national standards.

This document shall not be reproduced, except in full.

NATA Accredited Laboratory Number: 14965



R. K. Lock date 9/4/13

Surveyor
Legal Metrology Officer
for the Surveyor-General of NSW

Date of Verification: 6 Nov 2012
